

Links to GI May 25 Update



As we enter into the final stages of Links 2 GI, we want to thank you once again for your understanding and support while we complete these huge upgrades. In this month's update, we want to show the latest progress on Line Road and the Apirana/Pilkington/Tripoli roundabout.

In short



Works on **Line Road, between Eastview Road and Merfield Street**, are underway, with the speed tables completed, and footpath and cycleway being poured.



At the **roundabout**, all drainage works will be completed by the end of May, along with kerb and channel works from Pilkington Road onto Apirana Avenue.



We aim to start works on **Merton Road** in July 2025.



Line Road (Eastview Road - Merfield Street)

Having completed the majority of kerb and channel works between the Eastview Road and Merfield Street intersections, the upgrades are beginning to take shape!

The new raised crossing at the Line Road and Eastview Road intersection will help to improve safety for people walking and cycling.

The cycleway and footpath is being prepared and the initial concrete pours are underway.

Links to GI May 25 Update



Line Road & Eastview Road raised crossing






Line Road kerb and channel works underway



Links to GI May 25 Update



Upgrades at the Apirana/Pilkington/Tripoli roundabout will make it easier and safer for people to get to and from the Glen Innes Town Centre on foot or bike!

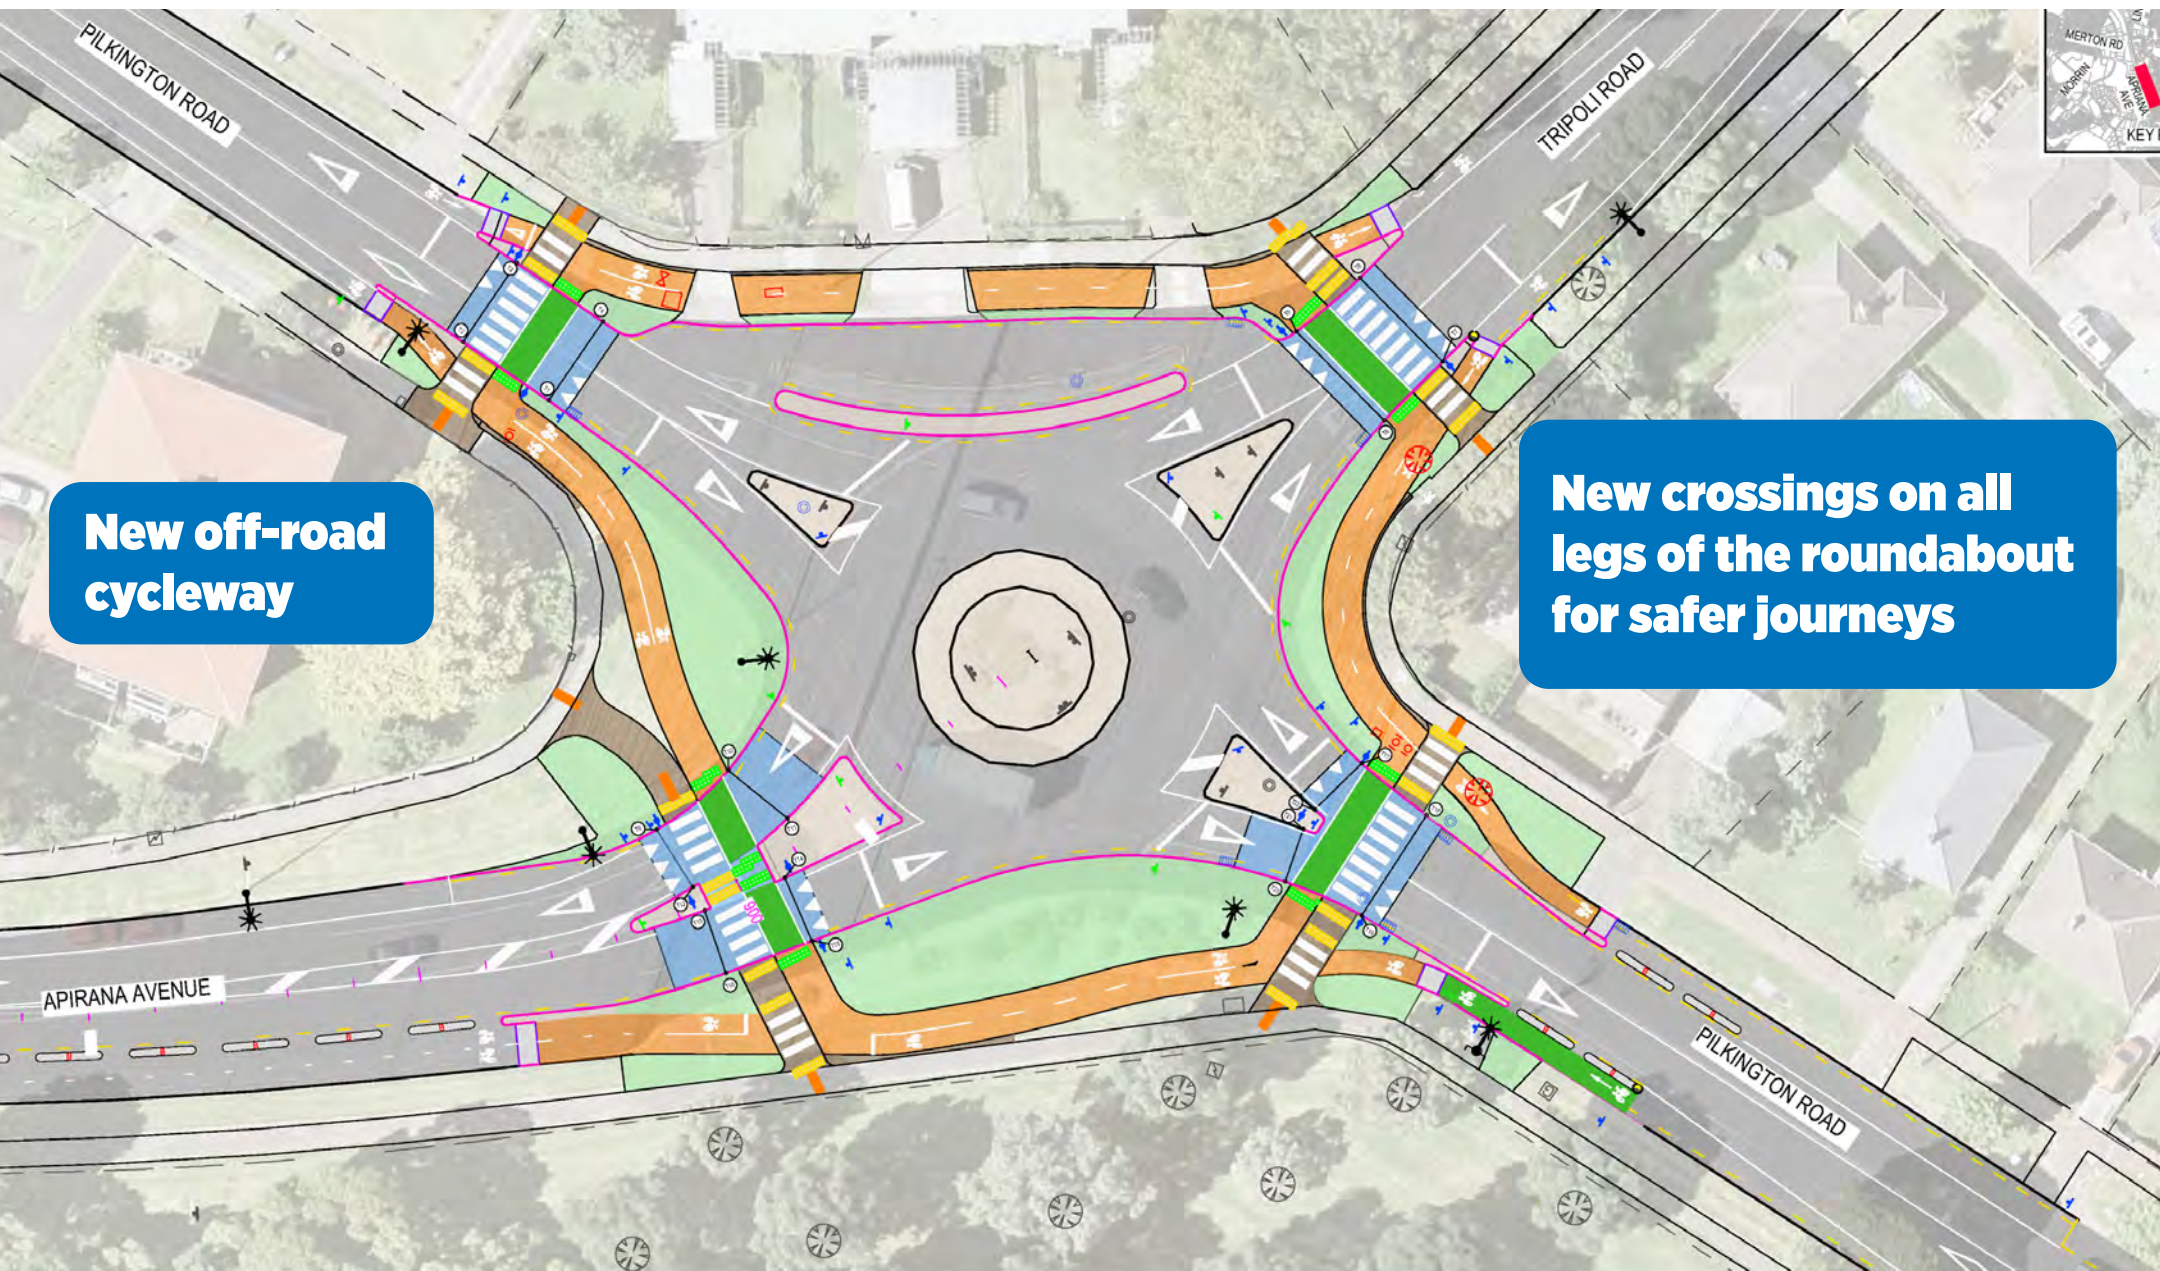



Apirana Avenue, Pilkington Road, and Tripoli Road roundabout progress

We're currently working on **stage 1 of 3** of the roundabout works and are finishing up the drainage works. We've installed three manholes, two catchpits, and 48 metres of stormwater pipes so far!

The Apirana Avenue south raised crossings have been prepared and excavated, and new traffic island kerbs are in place.



Apirana/Pilkington/Tripoli roundabout drainage works





Apirana/Pilkington/Tripoli stage one work area

Stage one is expected to be completed by the end of June 2025.





Apirana/Pilkington/Tripoli stage two work area


Once stage one has been completed, we will move to stage two which targets the southern side of the roundabout. More details coming soon.






Apirana/Pilkington/Tripoli stage three work area

More details on stage three coming soon.

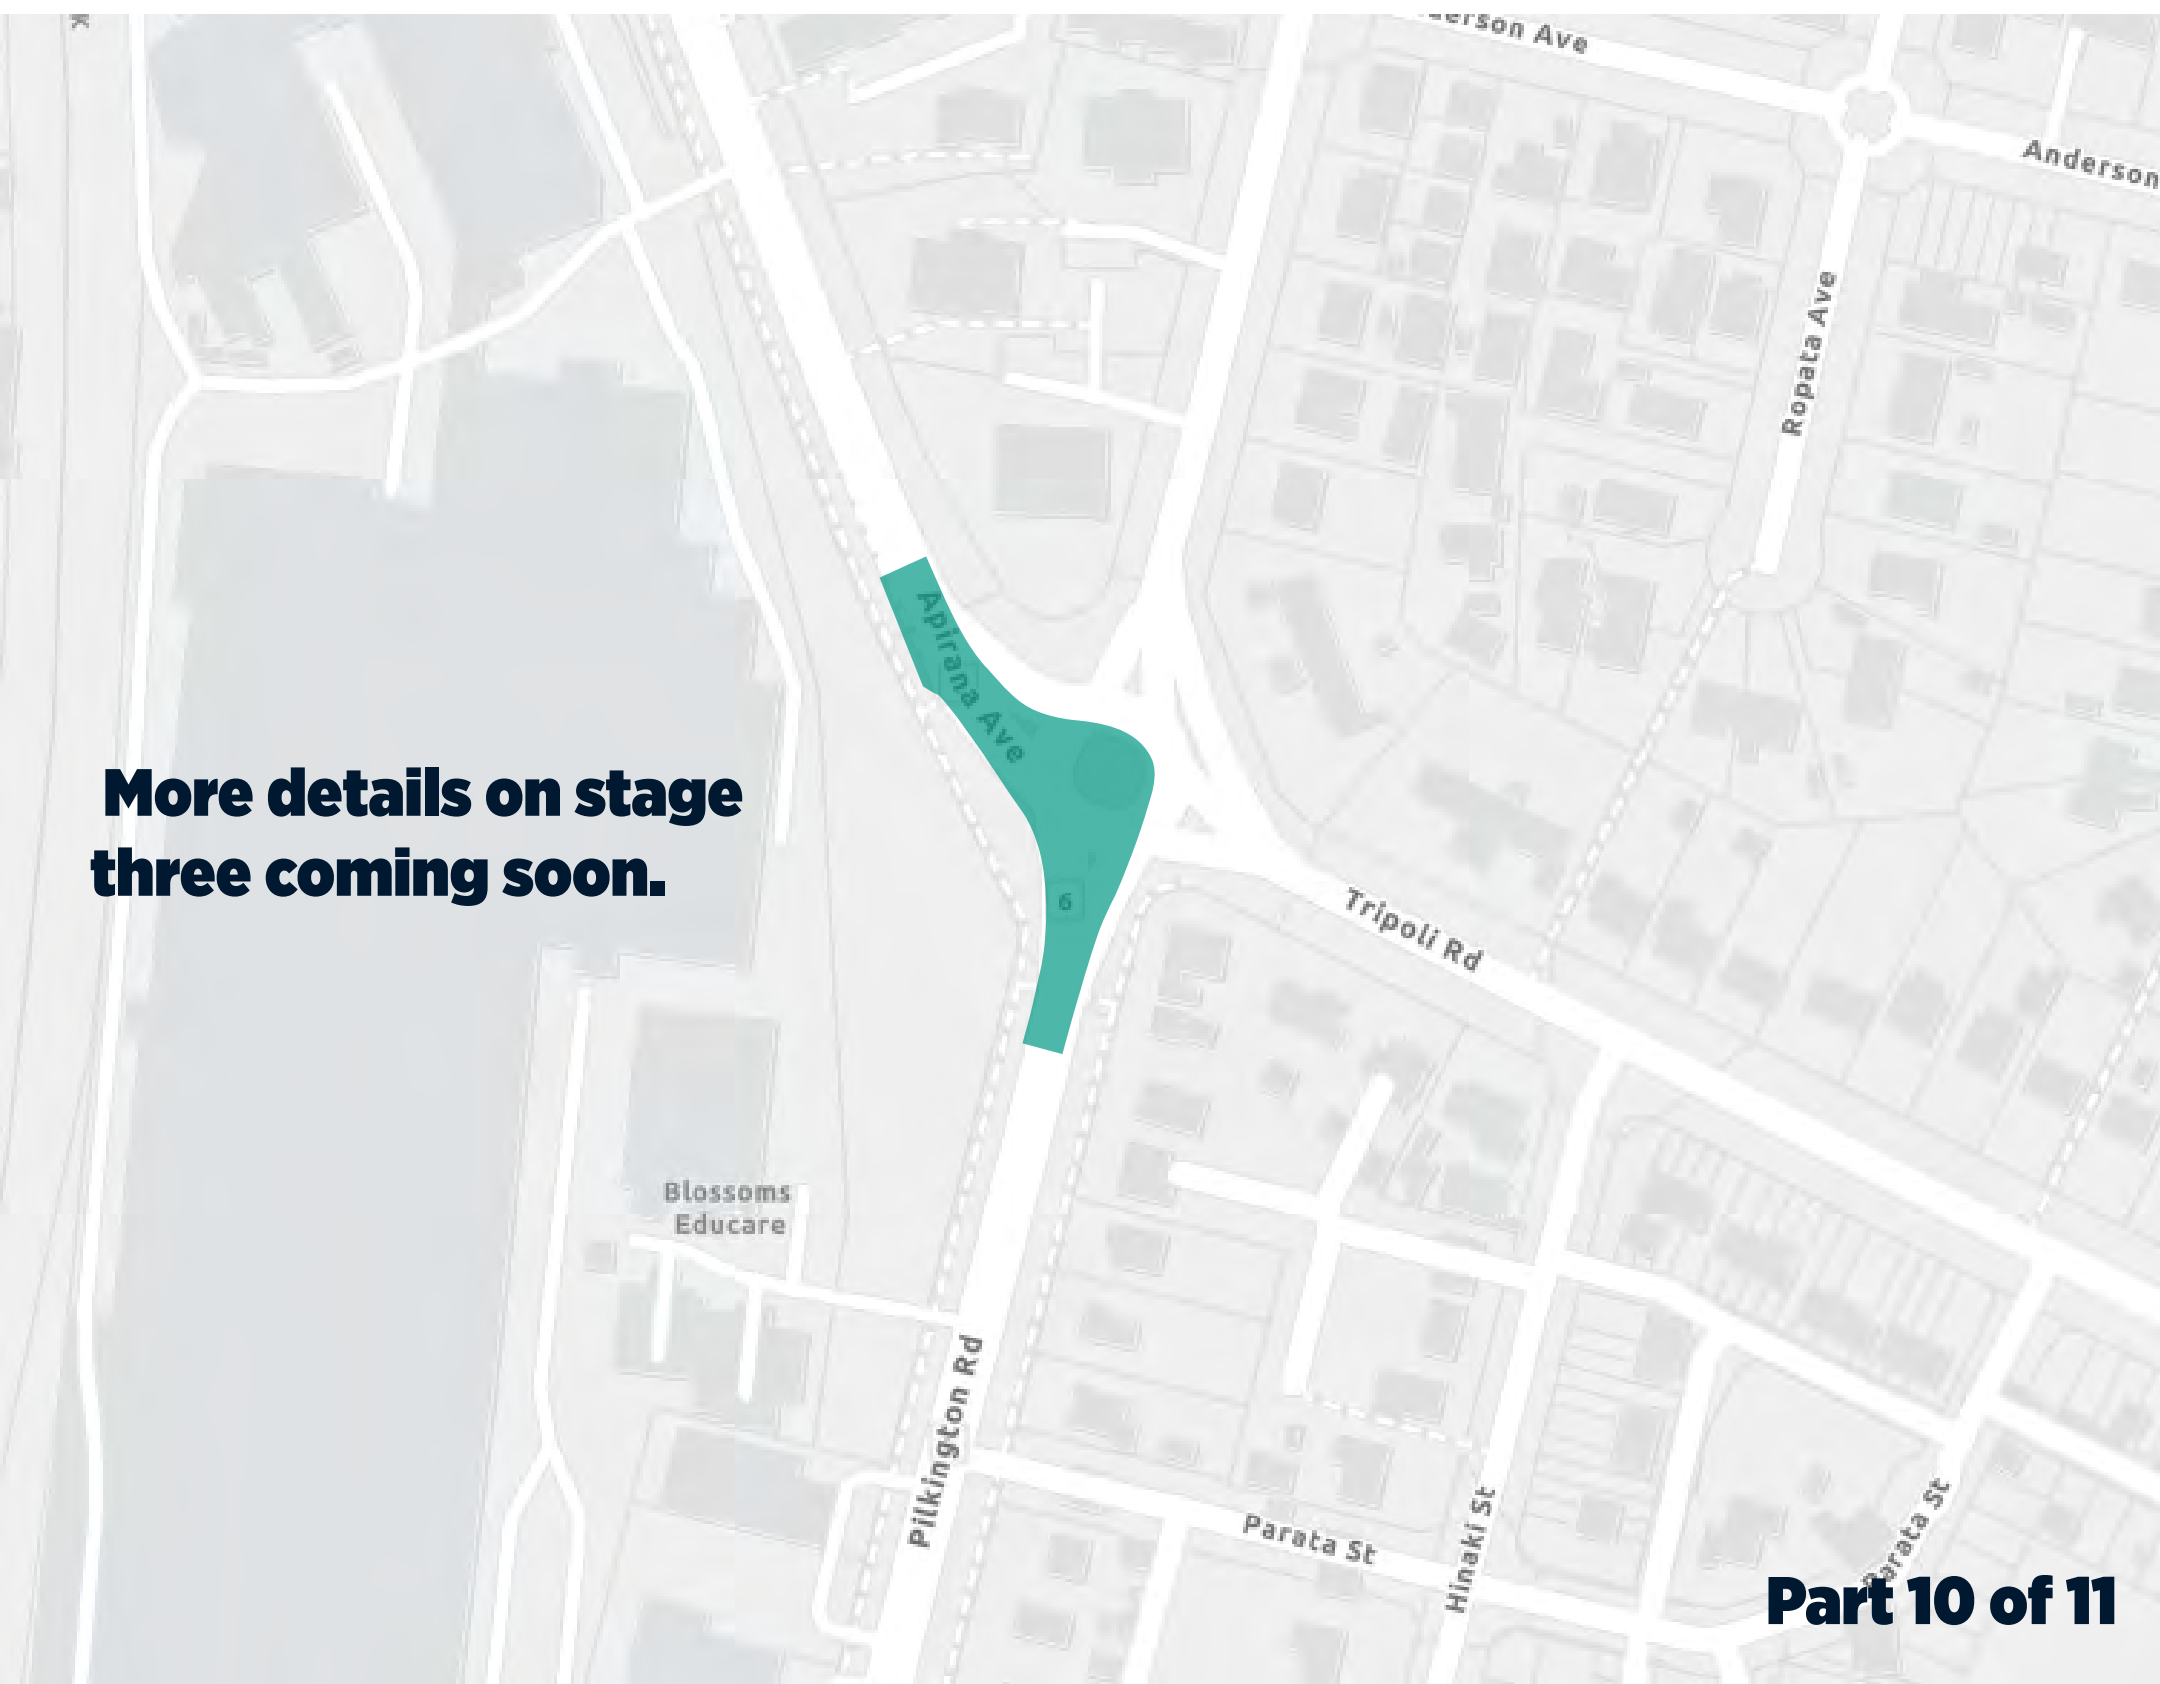





What's next



On Line Road, between Eastview Road and Merfield Street, we will be continuing excavation and starting the preparation and pouring of the new cycleway. Some trees have also been consented for removal in order to make the upgrades possible.



At the Apirana/Pilkington/Tripoli roundabout, kerb and channel works are to continue on Pilkington Road, heading onto Tripoli Road. Excavation and preparation work for the cycleway and Tripoli Road traffic island will also be underway soon.



We plan to start renewal works on Merton Road in July 2025, so keep an eye out for more updates!
